

**Bureau of Indian Education
Strategic Direction
Quarter 2 Progress Report**

As a result of a partial government shutdown, federal funding for the BIE expired on December 21, 2018 resulting in a shutdown of regular operations, including ongoing implementation of Year One Strategic Direction activities. During the duration of the shutdown, BIE personnel were either furloughed for the duration of the shutdown or, as required by law, only permitted to work on matters involving direct support of the safety and welfare of students or the orderly shutdown of operations.


The shutdown resulted in a delay of all work related to the implementation of the BIE's Year One Strategic Direction Milestones. All BIE Milestone teams will reassess work assignments upon the restoration of regular operations and make any necessary adjustments to ensure successful implementation of Year One Milestones.

Quarter 2 Progress Report Summary

Reporting ranged from 81% in October to 48% at the end of December. The deadline for December reporting occurred after the partial government shutdown. For the second quarter, 50 additional actions were scheduled to start and of those, 34 actions (68%) actually started and one action was completed.

Cumulatively by the end of December 2018, BIE had 278 actions planned for Year 1. Of the 278 actions, 133 actions (48%) were reported on. Digging deeper, 211 actions were scheduled to start between July and December and 181 actions (86%) actually started. Of the 181 actions started, 70 actions (39%) were reported on at the end of December. Of the 70 actions,

- 31 actions (44%) were reported as completed,
- 24 actions (34%) were reported on time, and
- 15 actions (21%) were reported as behind schedule.

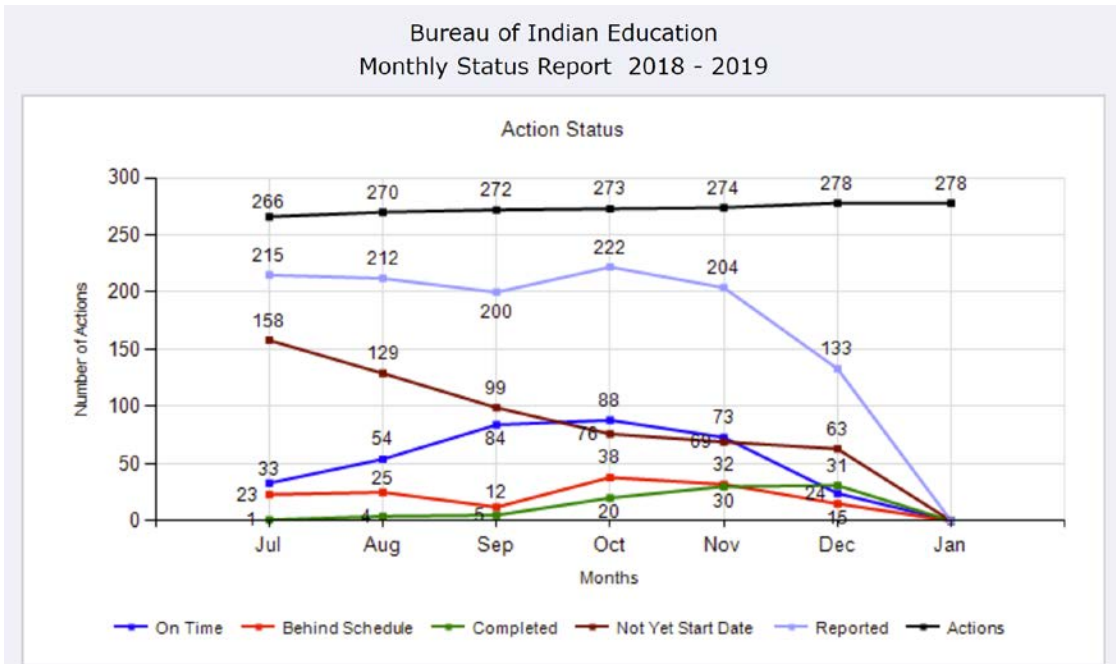

Highlights of work completed include:

- A template has been created to collect data on the existing Career and Technical Education Programs in all Bureau operated and Tribally controlled schools and TCS.


BIE Leadership and all BIE Milestone teams will reassess work assignments upon the restoration of regular operations and make any necessary adjustments to ensure successful implementation of Year One Milestones.

BIE Division Quarter 2 Progress Report

Office of the Director

Cumulatively, by the end of December 115 actions were assigned to this division and 39 actions (34%) were reported on. Of those 39 reported actions,

- 10 actions (26%) were reported as completed,
- 4 actions (10%) were reported as on time,
- No actions were reported as behind schedule, and
- 25 actions (64%) were reported as not yet started.

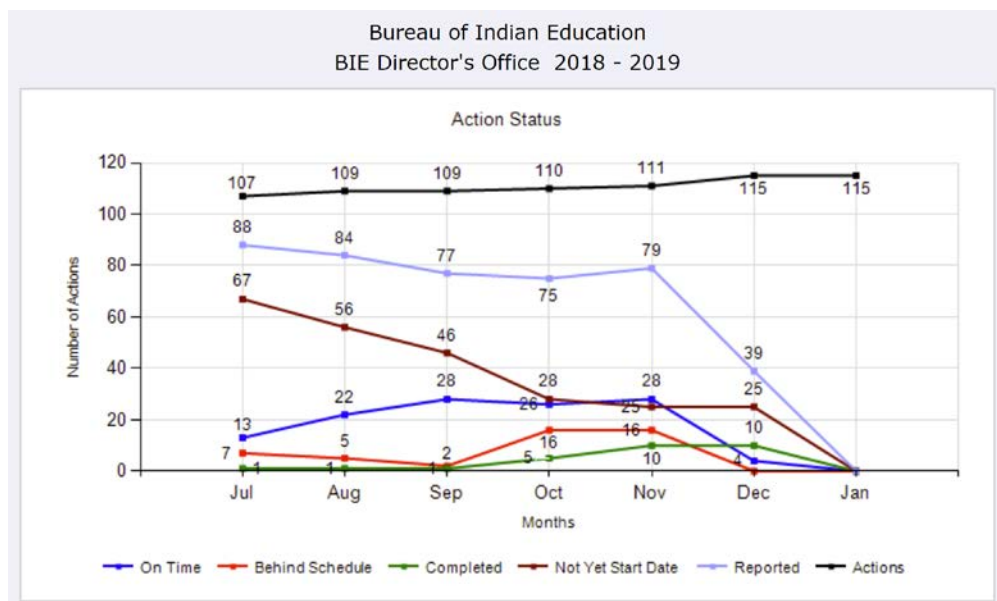


Bureau Operated Schools

Cumulatively, by the end of December 50 actions were assigned to this division and 31 actions (62%) were reported on. Of those 31 reported actions,

- 4 actions (13%) were reported as completed,
- 4 actions (13%) were reported as on time,
- 10 actions (32%) were reported as behind schedule, and
- 13 actions (42%) were reported as not yet started.

Bureau of Indian Education
Bureau Operated Schools 2018 - 2019

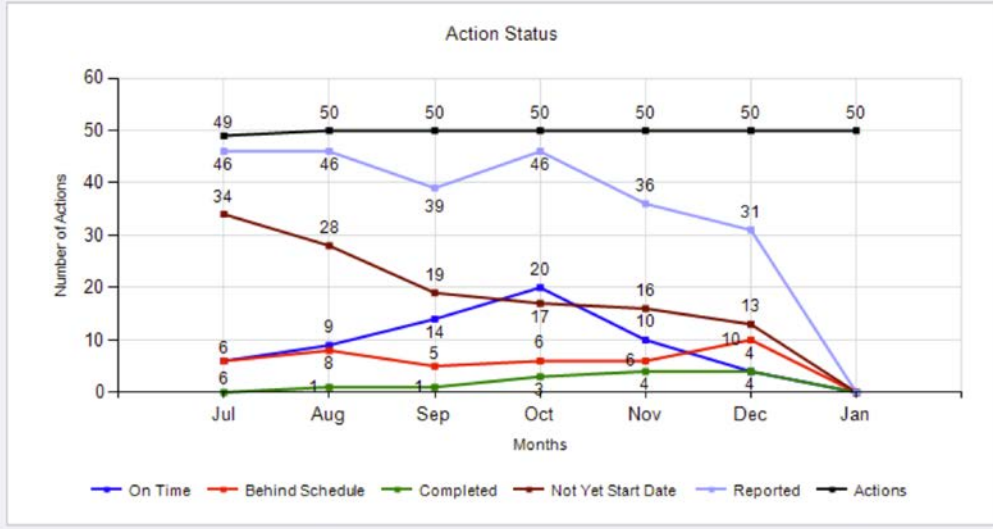


Navajo Schools

Cumulatively, by the end of December 42 actions were assigned to this division and 36 actions (86%) were reported on. Of those 36 reported actions,


- 11 actions (31%) were reported as completed,
- 11 actions (31%) were reported as on time,
- 5 actions (14%) were reported as behind schedule, and
- 9 actions (25%) were reported as not yet started.

Bureau of Indian Education
Navajo Schools 2018 - 2019

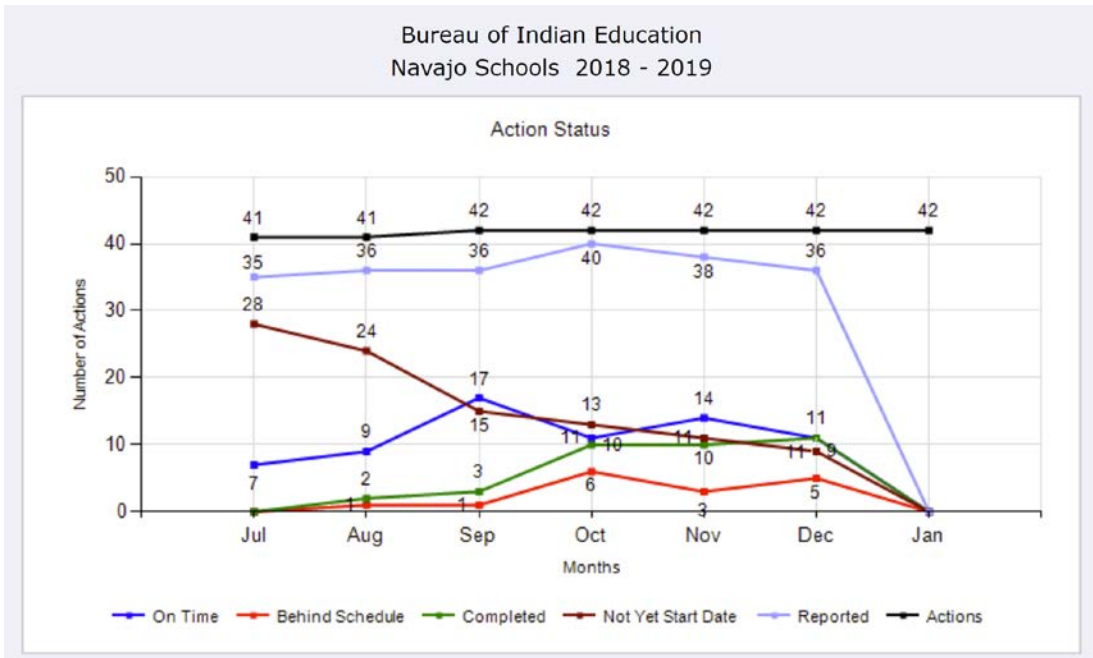

Performance & Accountability


Cumulatively, by the end of December 12 actions were assigned to this division and 3 actions (25%) were reported on. Those 3 actions were reported as not yet started.

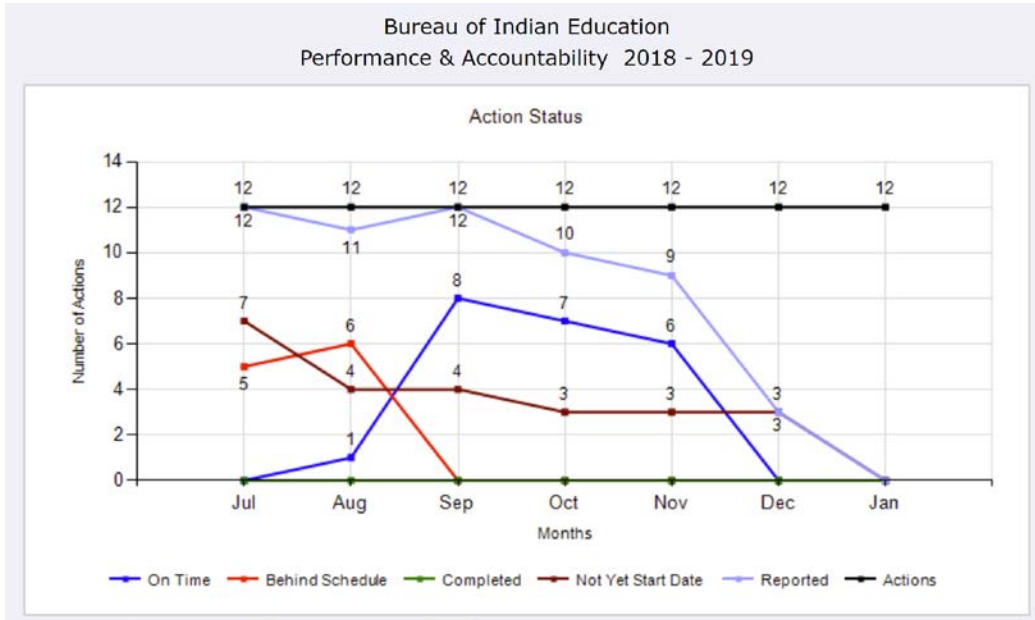

School Operations

Cumulatively, by the end of December 39 actions were assigned to this division and 10 actions (26%) were reported on. Of those 10 reported actions,

- 5 actions (50%) were reported as completed,
- No actions were reported as on time,
- No actions were reported as behind schedule, and
- 5 actions (50%) were reported as not yet started

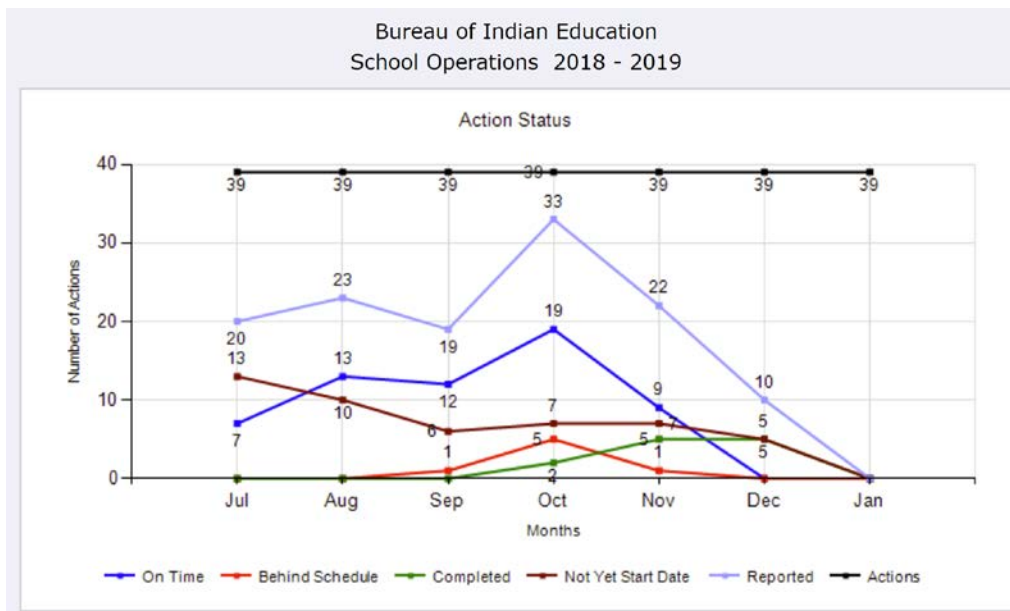

Tribally Controlled Schools

Cumulatively, by the end of December 20 actions were assigned to this division and 14 actions (70%) were reported on. Of those 14 reported actions,

- 1 action (7%) was reported as completed,
- 5 actions (36%) were reported as on time,
- No actions were reported as behind schedule, and
- 8 actions (57%) were reported as not yet started.

